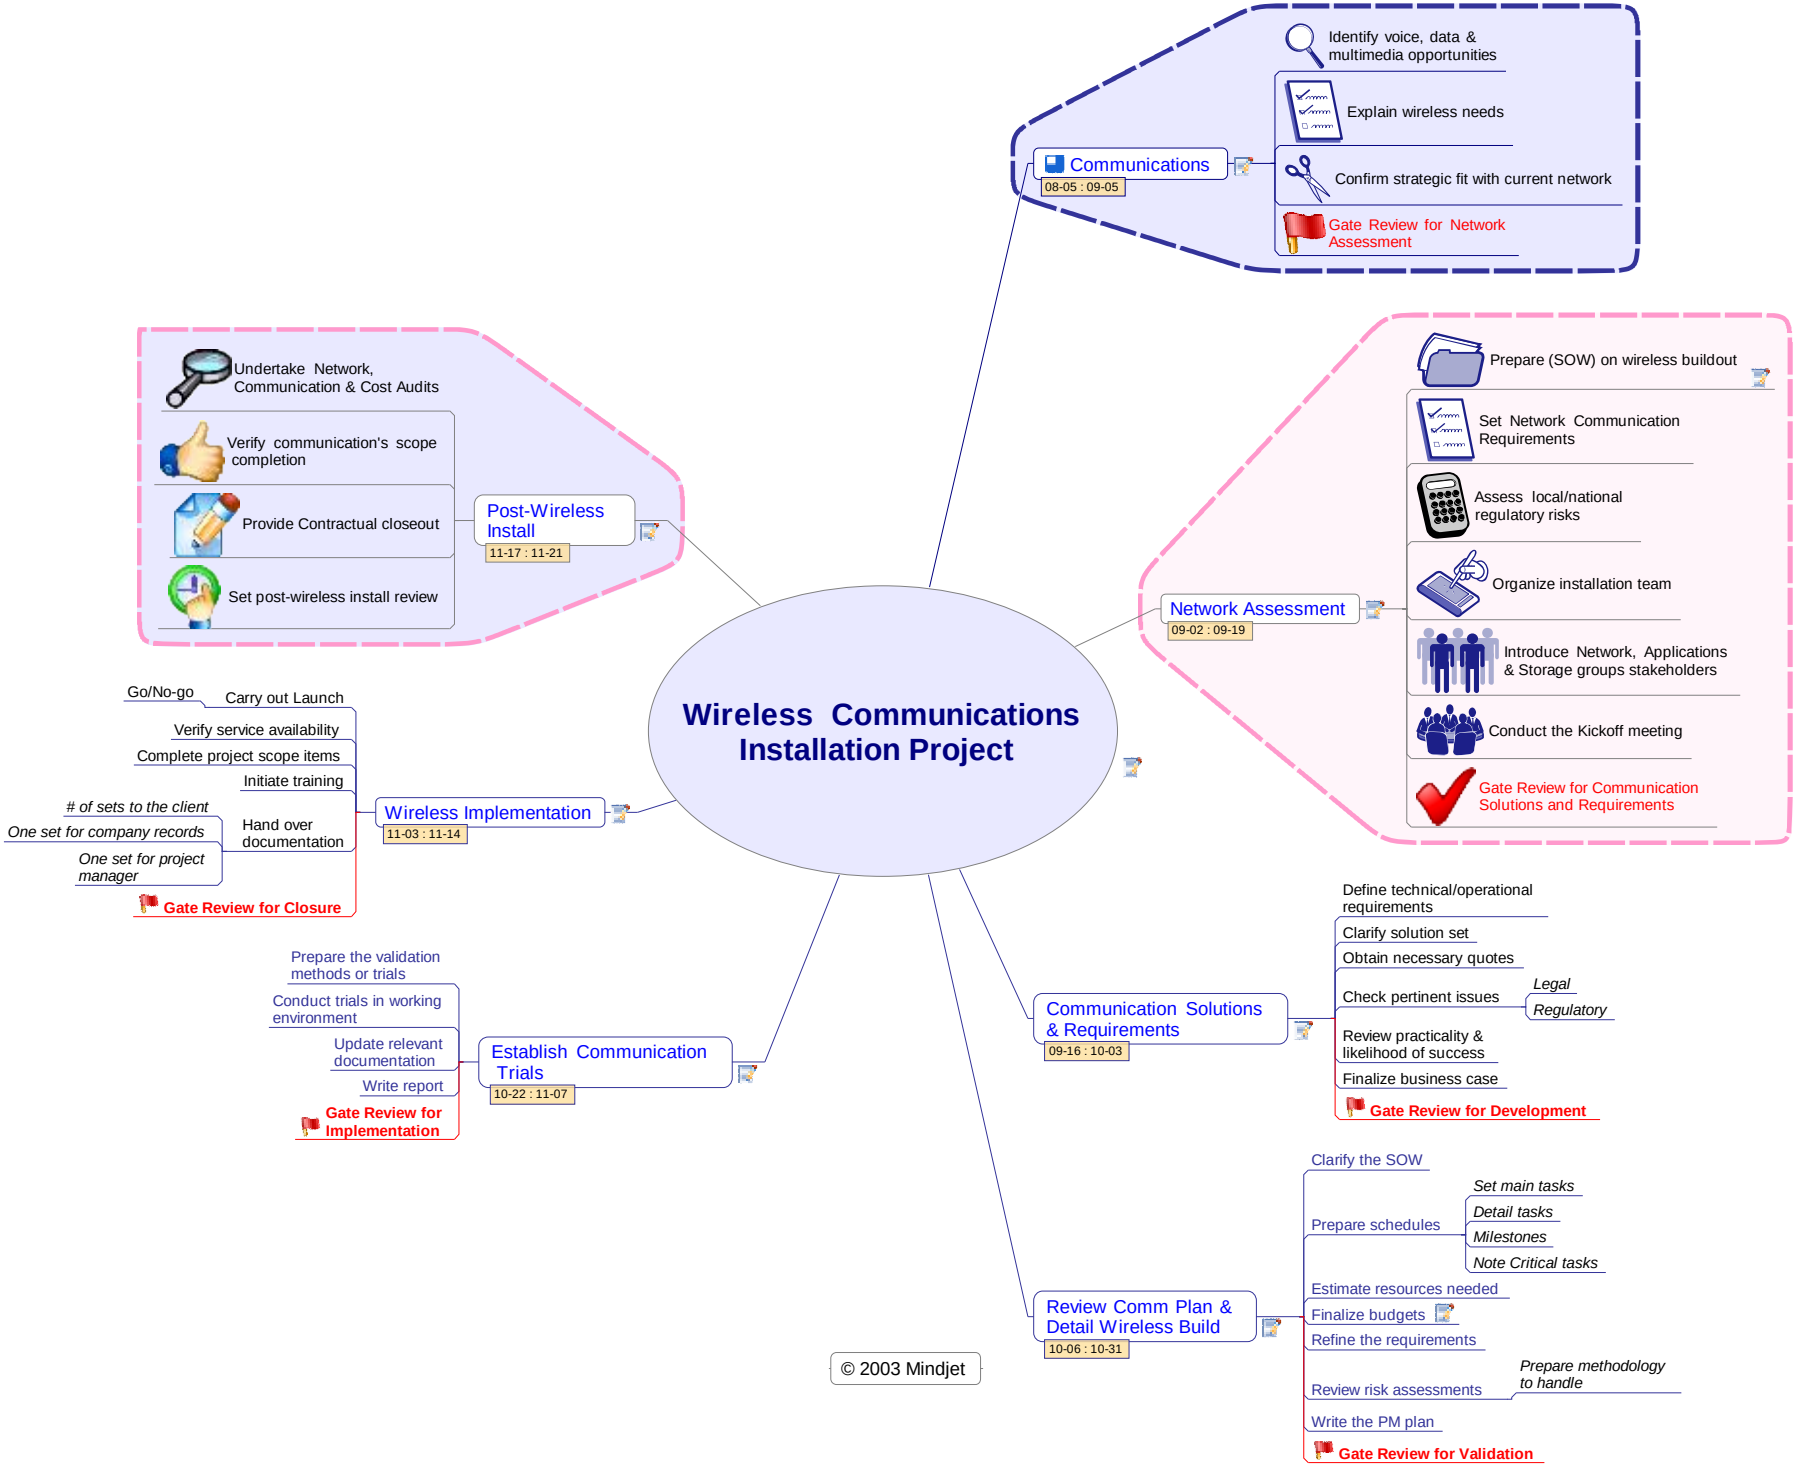
Wireless Communications Installation Project
Communications
08-05 : 09-05
Identify voice, data & multimedia opportunities
Explain wireless needs
Confirm strategic fit with current network
Gate Review for Network Assessment
Network Assessment
09-02 : 09-19
Prepare (SOW) on wireless buildout
Set Network Communication Requirements
Assess local/national regulatory risks
Organize installation team
Introduce Network, Applications & Storage groups stakeholders
Conduct the Kickoff meeting
Gate Review for Communication Solutions and Requirements
Communication Solutions & Requirements
09-16 : 10-03
Define technical/operational requirements
Clarify solution set
Obtain necessary quotes
Check pertinent issues
Legal
Regulatory
Review practicality & likelihood of success
Finalize business case
Gate Review for Development
Review Comm Plan & Detail Wireless Build
10-06 : 10-31
Clarify the SOW
Prepare schedules
Set main tasks
Detail tasks
Milestones
Note Critical tasks
Estimate resources needed
Finalize budgets
Refine the requirements
Review risk assessments
Prepare methodology to handle
Write the PM plan
Gate Review for Validation
Establish Communication Trials
10-22 : 11-07
Prepare the validation methods or trials
Conduct trials in working environment
Update relevant documentation
Write report
Gate Review for Implementation
Wireless Implementation
11-03 : 11-14
Carry out Launch
Go/No-go
Verify service availability
Complete project scope items
Initiate training
Hand over documentation
# of sets to the client
One set for company records
One set for project manager
Gate Review for Closure
Post-Wireless Install
11-17 : 11-21
Undertake Network, Communication & Cost Audits
Verify communication's scope completion
Provide Contractual closeout
Set post-wireless install review
© 2003 Mindjet
